




CANNELBURG ROAD (CR 900 E) PHASE 3: ROAD REHABILITATION



CURRENT OPERATIONS


July 2017:

The majority of earthwork and culvert pipe installation was completed between CR 800 N and CR 1000 N in June and July. Milestone Contractors are gearing up for a busy August.

WHAT'S NEXT

August 2017: August is set to be a busy month between CR 800 N and CR 1000 N with roadway cement stabilization starting at the beginning of the month and concrete paving finishing out the month.

CR 1000 North will close at CR 900 E for 30 days starting on August 7 for reconstruction of the intersection. The official detour for CR 900 E will change to the following routes at that time: SR 58 to CR 700 E to CR 1000 N to CR 675 E to CR 925 N to CR 650 E to CR 800 N.

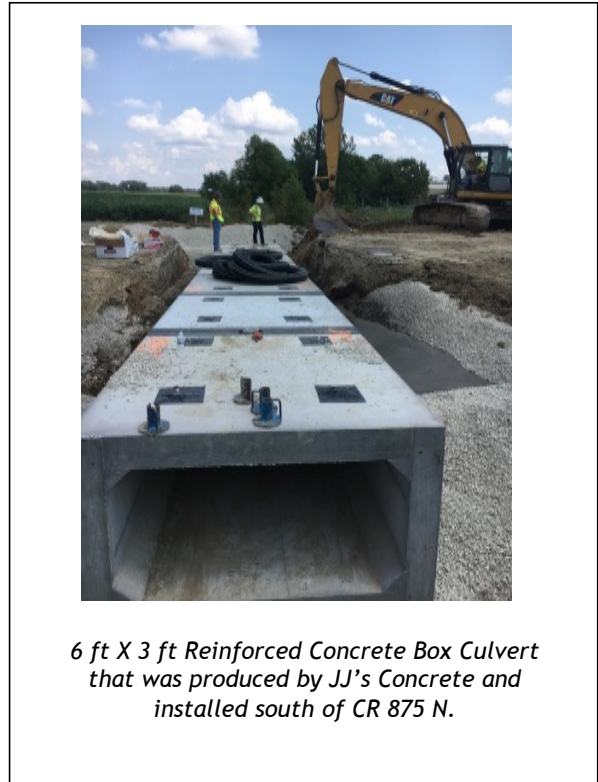

6 ft X 3 ft Reinforced Concrete Box Culvert that was produced by JJ's Concrete and installed south of CR 875 N.



Donut Hill received a makeover throughout the month of July!

PROJECT DESCRIPTION

The project involves the reconstruction of Cannelburg Road with concrete travel lanes and asphalt shoulders from 330 feet north of CR 800 N to 1250 N (Park Street) in Odon

Contract No.: R-37248

Start Date: On or After May 16, 2017

Completion Date: June 7, 2019

Daviss County Highway Department
Phone: 1-812-444-5798

On Site Project Engineer: Jason Heile
Email: daviesseng@gmail.com

Contractor: Milestone Contractors, L.P.
Contractor Supervisor: Travis Caswell

A Daviss County Project for more information
Visit www.daviss.org

or follow us on Facebook or twitter
Facebook Daviss County Indiana: Highway Department
Twitter @daviesscohwydep
